

Installation of GBF's at Thorntonbank situation on 20-10-2008

D1


Completed as per DAR	
Foundation pit bulk dredging	8-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	11-04-2008
Gravel bed top layer	20-04-2008
GBF Installed	26/27-04-2008
Backfill	11-05-2008
Infill	14-08-2008
Scour protection filter layer	
Scour protection armour layer	
Armour layer on cables	
Ladders	10-07-2008
Levelling transition piece	10-07-2008
Dry infill of last 2m	15-09-2008
Fairly airtight floor installed	10-07-2008
service crane base	10-07-2008
33 kV Blind flanges bellmouths + J-tubes	09-10-2008
Installation external J-tubes	
Measurement Earth Resistance	20-08-2008

D2

Completed as per DAR	
Foundation pit bulk dredging	9-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	12-04-2008
Gravel bed top layer	20-04-2008
GBF Installed	7/8-05-2008
Backfill	24-05-2008
Infill	17-08-2008
Scour protection filter layer	22-08-2008
Scour protection armour layer	
Armour layer on cables	
Ladders	17-08-2008
Levelling transition piece	17-06-2008
Dry infill of last 2m	17-06-2008
Fairly airtight floor closed	18-06-2008
service crane base	17-06-2008
Blind flanges bellmouths	
Installation external J-tubes	
Measurement Earth Resistance	28-08-2008

D3

Completed as per DAR	
Foundation pit bulk dredging	21-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	10-04-2008
Gravel bed top layer	24-04-2008
GBF Installed	21/22-05-2008
Backfill	5-06-2008
Infill	28-07-2008
Scour protection filter layer	15-08-2008
Scour protection armour layer	
Armour layer on cables	
Ladders	31-07-2008
Levelling transition piece	30-07-2008
Dry infill of last 2m	31-07-2008
Fairly airtight floor	
service crane base	30-07-2008
concrete wall damage repaired on	31-07-2008
Blind flanges bellmouths	09-10-2008
Installation external J-tubes	
Measurement Earth Resistance	30-08-2008

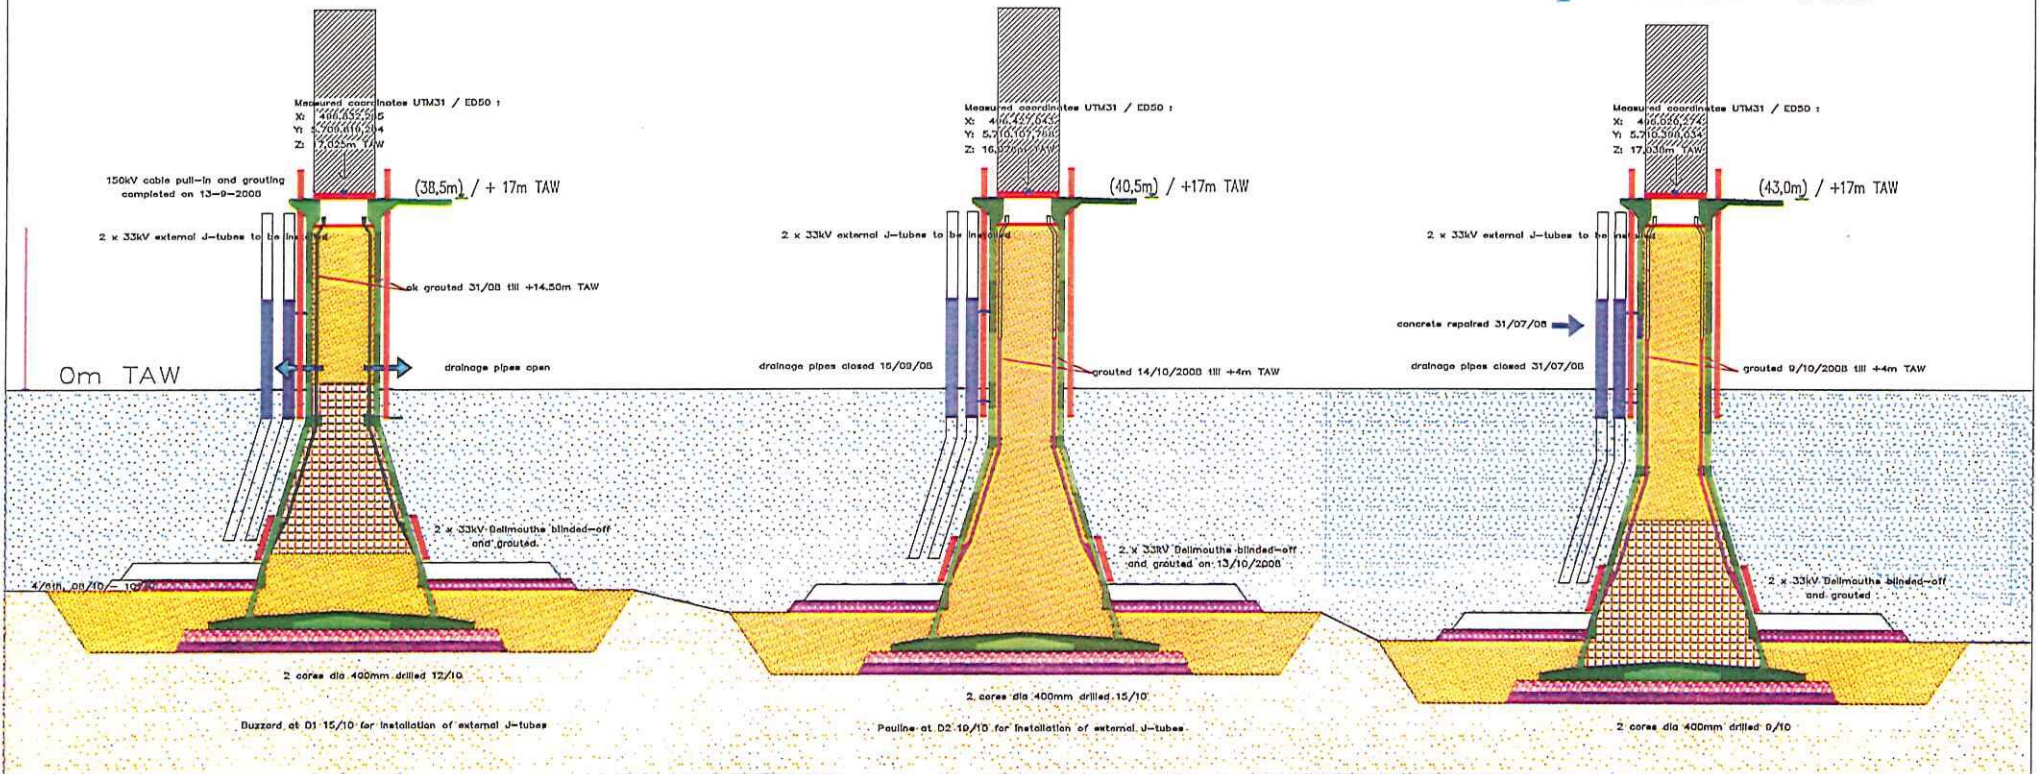

■ Finalized
■ Ongoing / Partially realized

■ Infill with big bags
■ Infill with big bags (magna dense)
■ Hydraulic infill

■ Installation of external 33kV J-tubes started

Installation of GBF's at Thorntonbank situation on 20-10-2008

D4




	Completed as per DAR
Foundation pit bulk dredging	23-03-2008
Foundation pit precision dredging	4-05-2008
Gravel bed filter layer	13-05-2008
Gravel bed top layer	17-05-2008
GBF installed	22/23-05-2008
WackiH	18-06-2008
Infill	25-07-2008
Scour protection filter layer	20-09-2008
Armour layer on cables	
Ladders	18-08-2008
Leveling transition piece	18-08-2008
Dry fill of last 2m	17-08-2008
Fairly airtight floor	
service crane bents	19-09-2008
Blind flange bellmouths	22-08-2008
Grouted J-tubes	25-09-2008
Final works boat landing	
Installation external J-tubes	
Measurement Earth Resistance	28-05-2008

D5

	Completed as per DAR
Foundation pit bulk dredging	23-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	9-05-2008
Gravel bed top layer	12-05-2008
GBF installed	30/31-05-2008
WackiH	11-06-2008
Infill	3-07-2008
Scour protection filter layer	31-08-2008
Armour layer on cables	
Ladders	4-07-2008
Leveling transition piece	30-05-2008
Dry fill of last 2m	3-07-2008
Fairly airtight floor	
service crane bents	30-06-2008
Blind flange bellmouths	28-09-2008
Installation external J-tubes	
Measurement Earth Resistance	30-08-2008

D6

	Completed as per DAR
Foundation pit bulk dredging	2-04-2008
Foundation pit precision dredging	5-04-2008
Gravel bed filter layer	6-05-2008
Gravel bed top layer	12-05-2008
GBF installed	26/29-05-2008
WackiH	14-06-2008
Heavy Infill	22-08-2008
Soil Infill	27-09-2008
Scour protection filter layer	28-09-2008
Armour layer on cables	
Ladders	25-09-2008
Leveling transition piece	29-09-2008
Dry fill of last 2m	27-09-2008
Fairly airtight floor	
service crane bents	28-09-2008
Blind flange bellmouth	11-10-2008
Installation external J-tubes	
Measurement Earth Resistance	30-08-2008

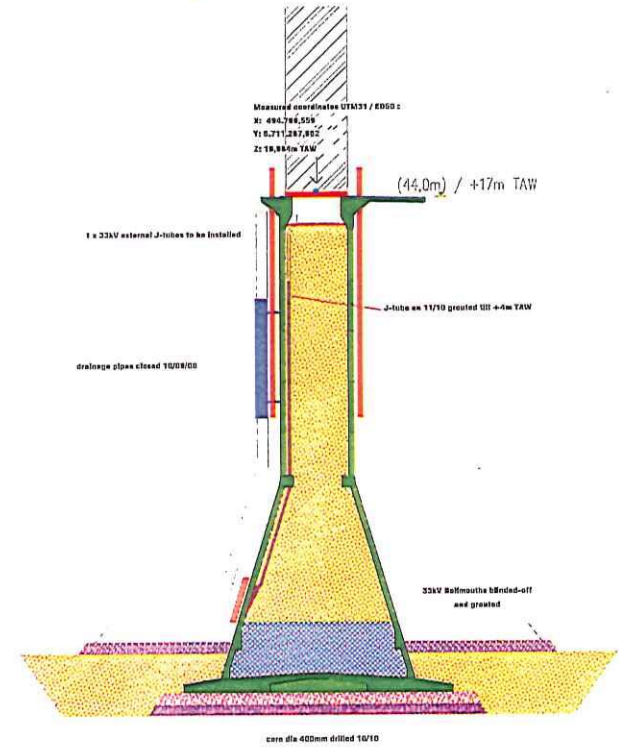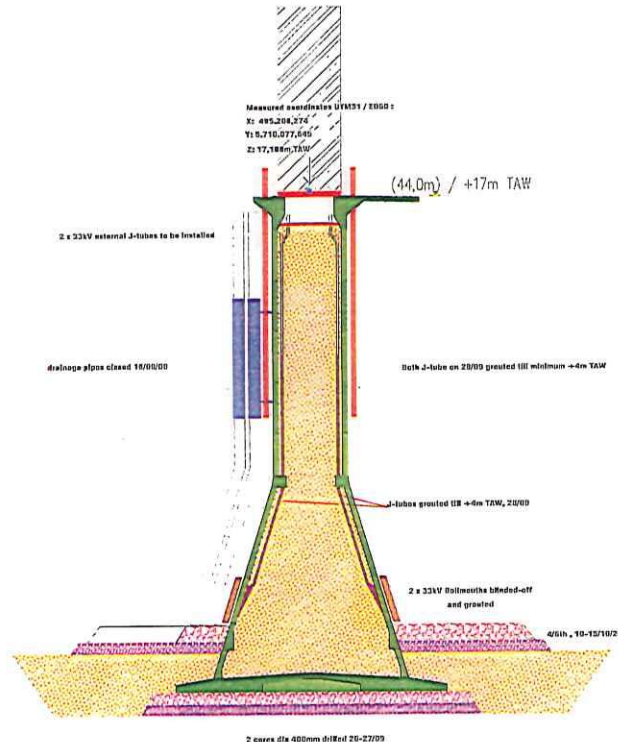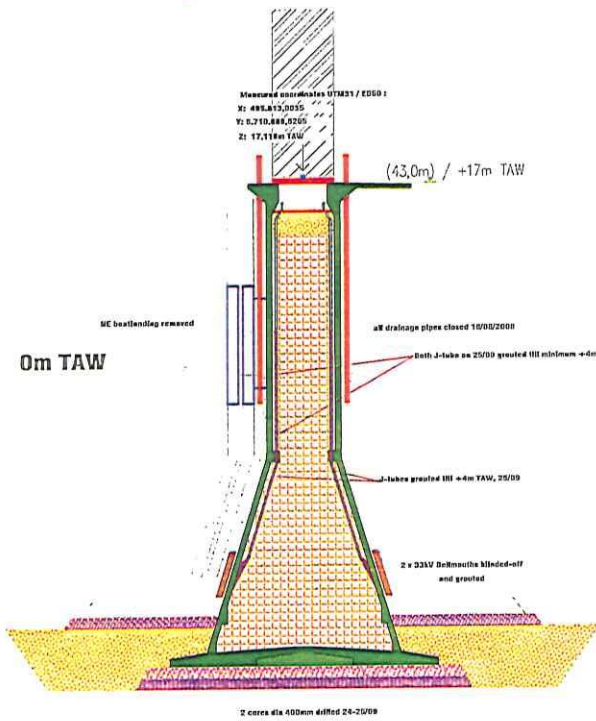

- Finalized
- Ongoing / Partially realized

- Infill with big bags
- Infill with big bags (magna dense)
- Hydraulic infill

Installation of external 33kV J-tubes started
