

Installation of GBF's at Thorntonbank situation on 23-06-2008

D1


- | | |
|---|---------------|
| Completed as per DAR | |
| <input checked="" type="checkbox"/> Foundation pit bulk dredging | 8-03-2008 |
| <input checked="" type="checkbox"/> Foundation pit precision dredging | 4-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed filter layer | 11-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed top layer | 20-04-2008 |
| <input checked="" type="checkbox"/> GBF installed | 26/27-04-2008 |
| <input checked="" type="checkbox"/> Backfill | 11-05-2008 |
| <input type="checkbox"/> Infill | |
| <input type="checkbox"/> Scour protection filter layer | |
| <input type="checkbox"/> Scour protection armour layer | |
| <input type="checkbox"/> Armour layer on cables | |
| <input type="checkbox"/> Ladders | |
| <input type="checkbox"/> Levelling transition piece | |
| <input type="checkbox"/> Dry infill of last 2m | |
| <input type="checkbox"/> Fairly airtight floor | |

D2

- | | |
|---|-------------|
| Completed as per DAR | |
| <input checked="" type="checkbox"/> Foundation pit bulk dredging | 9-03-2008 |
| <input checked="" type="checkbox"/> Foundation pit precision dredging | 4-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed filter layer | 12-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed top layer | 20-04-2008 |
| <input checked="" type="checkbox"/> GBF installed | 7/8-05-2008 |
| <input checked="" type="checkbox"/> Backfill | 24-05-2008 |
| <input checked="" type="checkbox"/> Infill | 17-06-2008 |
| <input type="checkbox"/> Scour protection filter layer | |
| <input type="checkbox"/> Scour protection armour layer | |
| <input type="checkbox"/> Armour layer on cables | |
| <input type="checkbox"/> Ladders | 17-06-2008 |
| <input type="checkbox"/> Levelling transition piece | 17-06-2008 |
| <input type="checkbox"/> Dry infill of last 2m | 17-06-2008 |
| <input type="checkbox"/> Fairly airtight floor | 18-06-2008 |
| <input type="checkbox"/> service crane base | 17-06-2008 |

D3

- | | |
|---|---------------|
| Completed as per DAR | |
| <input checked="" type="checkbox"/> Foundation pit bulk dredging | 21-03-2008 |
| <input checked="" type="checkbox"/> Foundation pit precision dredging | 4-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed filter layer | 19-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed top layer | 24-04-2008 |
| <input checked="" type="checkbox"/> GBF installed | 21/22-05-2008 |
| <input checked="" type="checkbox"/> Backfill | 5-06-2008 |
| <input type="checkbox"/> Infill | |
| <input type="checkbox"/> Scour protection filter layer | |
| <input type="checkbox"/> Scour protection armour layer | |
| <input type="checkbox"/> Armour layer on cables | |
| <input type="checkbox"/> Ladders | |
| <input type="checkbox"/> Levelling transition piece | |
| <input type="checkbox"/> Dry infill of last 2m | |
| <input type="checkbox"/> Fairly airtight floor | |
| <input type="checkbox"/> service crane base | |

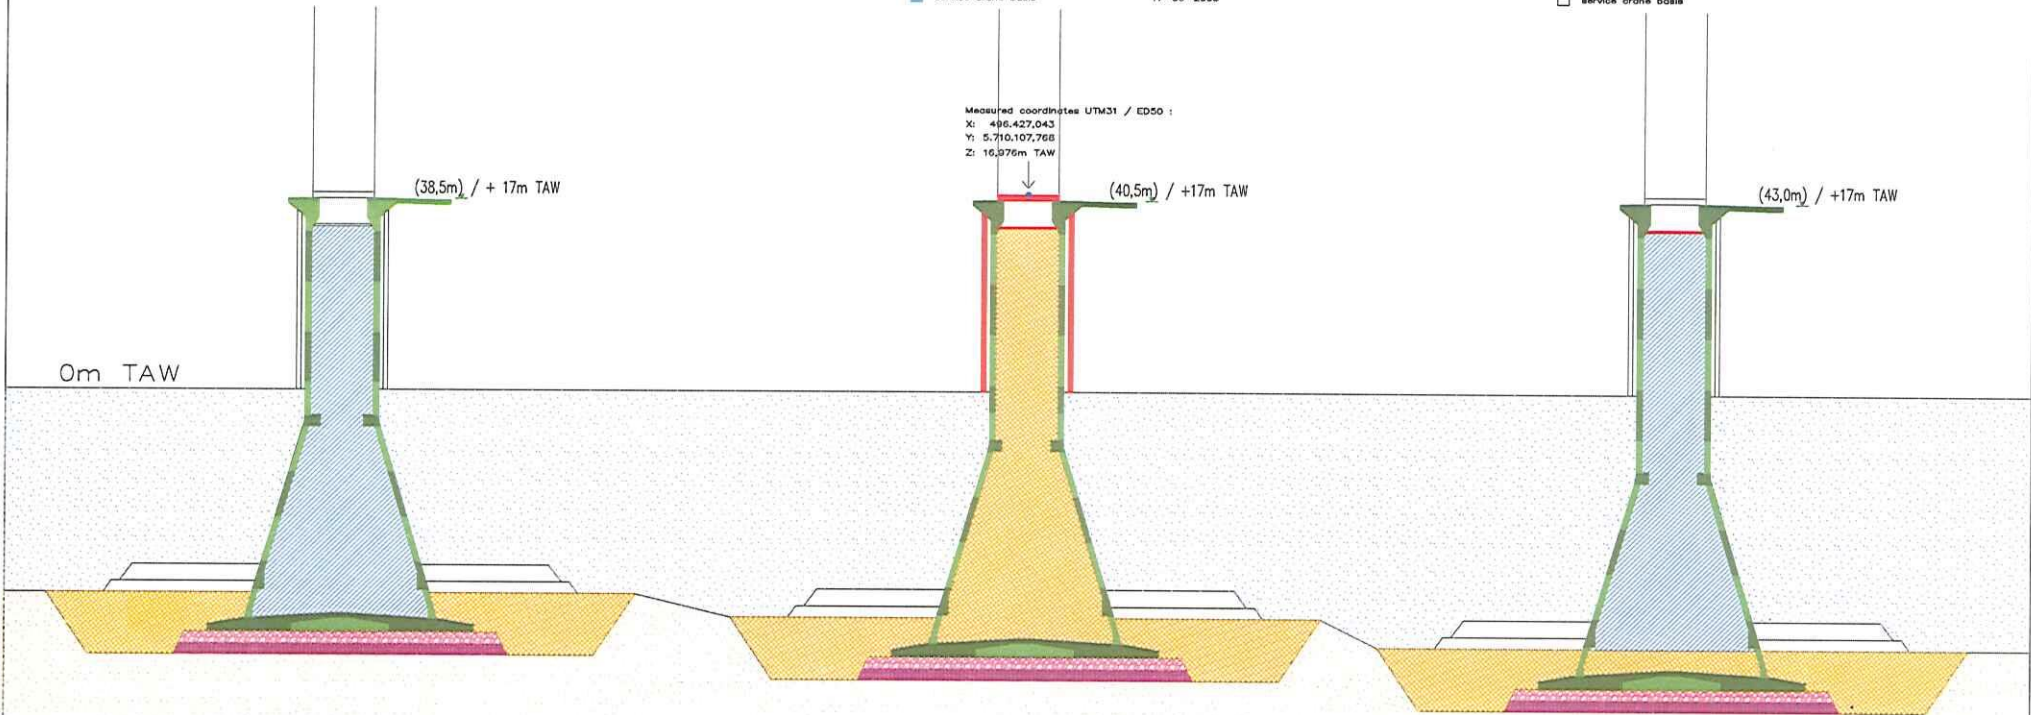

- Finalized
- Ongoing / Partially realized

Installation of GBF's at Thorntonbank situation on 23-06-2008

D4


- | | |
|---|----------------------|
| | Completed as per DAR |
| <input checked="" type="checkbox"/> Foundation pit bulk dredging | 23-03-2008 |
| <input checked="" type="checkbox"/> Foundation pit precision dredging | 4-05-2008 |
| <input checked="" type="checkbox"/> Gravel bed filter layer | 13-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed top layer | 17-04-2008 |
| <input checked="" type="checkbox"/> GBF installed | 22/23-05-2008 |
| <input checked="" type="checkbox"/> Backfill | 16-06-2008 |
| <input type="checkbox"/> Infill | |
| <input type="checkbox"/> Scour protection filter layer | |
| <input type="checkbox"/> Scour protection armour layer | |
| <input type="checkbox"/> Armour layer on cables | |
| <input type="checkbox"/> Ladders | |
| <input type="checkbox"/> Levelling transition piece | |
| <input type="checkbox"/> Dry infill of last 2m | |
| <input checked="" type="checkbox"/> Fairly airtight floor | |

D5

- | | |
|---|----------------------|
| | Completed as per DAR |
| <input checked="" type="checkbox"/> Foundation pit bulk dredging | 23-03-2008 |
| <input checked="" type="checkbox"/> Foundation pit precision dredging | 4-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed filter layer | 9-05-2008 |
| <input checked="" type="checkbox"/> Gravel bed top layer | 12-05-2008 |
| <input checked="" type="checkbox"/> GBF installed | 30/31-05-2008 |
| <input checked="" type="checkbox"/> Backfill | 11-08-2008 |
| <input type="checkbox"/> Infill | |
| <input type="checkbox"/> Scour protection filter layer | |
| <input type="checkbox"/> Scour protection armour layer | |
| <input type="checkbox"/> Armour layer on cables | |
| <input type="checkbox"/> Ladders | |
| <input type="checkbox"/> Levelling transition piece | |
| <input type="checkbox"/> Dry infill of last 2m | |
| <input checked="" type="checkbox"/> Fairly airtight floor | |

D6

- | | |
|---|----------------------|
| | Completed as per DAR |
| <input checked="" type="checkbox"/> Foundation pit bulk dredging | 2-04-2008 |
| <input checked="" type="checkbox"/> Foundation pit precision dredging | 5-04-2008 |
| <input checked="" type="checkbox"/> Gravel bed filter layer | 6-05-2008 |
| <input checked="" type="checkbox"/> Gravel bed top layer | 12-05-2008 |
| <input checked="" type="checkbox"/> GBF installed | 28/29-05-2008 |
| <input checked="" type="checkbox"/> Backfill | 14-06-2008 |
| <input checked="" type="checkbox"/> Heavy infill | 22-06-2008 |
| <input type="checkbox"/> Sand infill | |
| <input type="checkbox"/> Scour protection filter layer | |
| <input type="checkbox"/> Scour protection armour layer | |
| <input type="checkbox"/> Armour layer on cables | |
| <input checked="" type="checkbox"/> Ladders | |
| <input type="checkbox"/> Levelling transition piece | |
| <input type="checkbox"/> Dry infill of last 2m | |
| <input checked="" type="checkbox"/> Fairly airtight floor | |

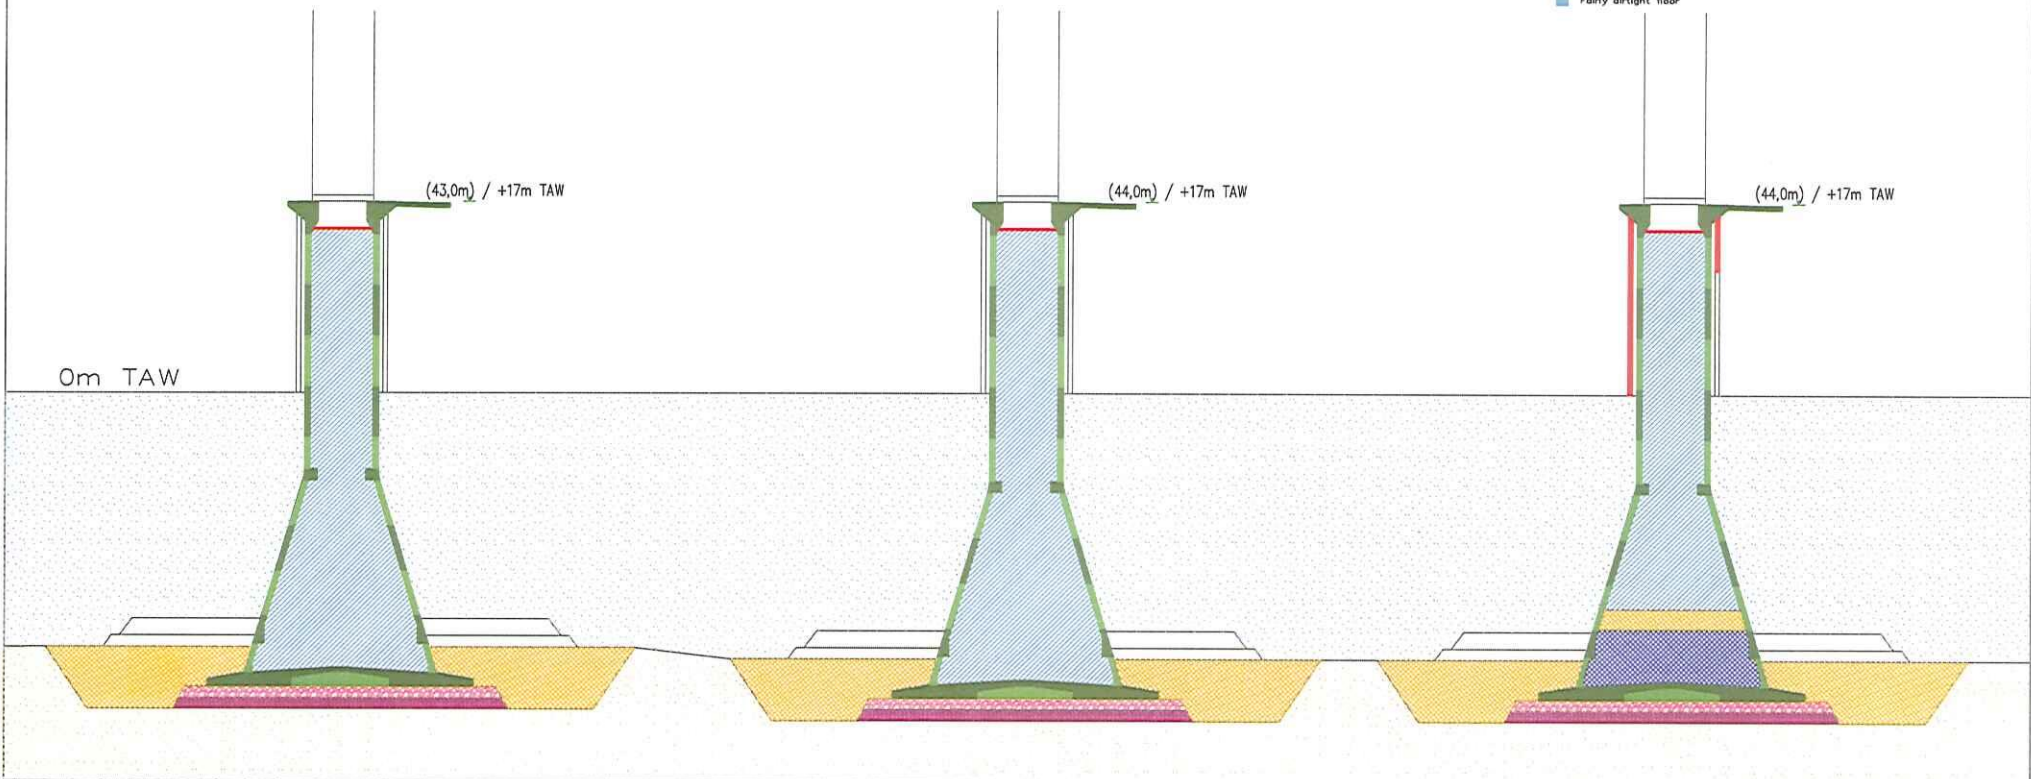

- Finalized
- Ongoing / Partially realized
