

Installation of GBF's at Thorntonbank situation on 13-10-2008

D1


Completed as per DAR	
Foundation pit bulk dredging	8-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	11-04-2008
Gravel bed top layer	20-04-2008
GBF installed	28/27-04-2008
Backfill	11-05-2008
fill	14-05-2008
Scour protection filter layer	
Scour protection armour layer	
Armour layer on cables	
Ladders	10-07-2008
Leveling transition piece	10-07-2008
Dry fill of last 2m	15-08-2008
Fairly airtight floor installed	10-07-2008
service crane base	10-07-2008
33 kV Blind flanges bellmouths + J-tubes grouted	31-08-2008
Installation external J-tubes	
Measurement Earth Resistance	29-08-2008

D2

Completed as per DAR	
Foundation pit bulk dredging	8-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	12-04-2008
Gravel bed top layer	20-04-2008
GBF installed	7/8-05-2008
Backfill	24-05-2008
fill	17-06-2008
Scour protection filter layer	22-09-2008
Scour protection armour layer	
Armour layer on cables	
Ladders	17-06-2008
Leveling transition piece	17-06-2008
Dry fill of last 2m	17-08-2008
Fairly airtight floor closed	18-08-2008
service crane base	17-06-2008
Blind flanges bellmouths	
Installation external J-tubes	
Measurement Earth Resistance	28-08-2008

D3

Completed as per DAR	
Foundation pit bulk dredging	21-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	19-04-2008
Gravel bed top layer	24-04-2008
GBF installed	21/22-05-2008
Backfill	5-06-2008
fill	29-07-2008
Scour protection filter layer	15-08-2008
Scour protection armour layer	
Armour layer on cables	
Ladders	31-07-2008
Leveling transition piece	30-07-2008
Dry fill of last 2m	31-07-2008
Fairly airtight floor	
service crane base	30-07-2008
concrete wall damage repaired on	31-07-2008
Blind flanges bellmouths	08-10-2008
Installation external J-tubes	
Measurement Earth Resistance	30-08-2008

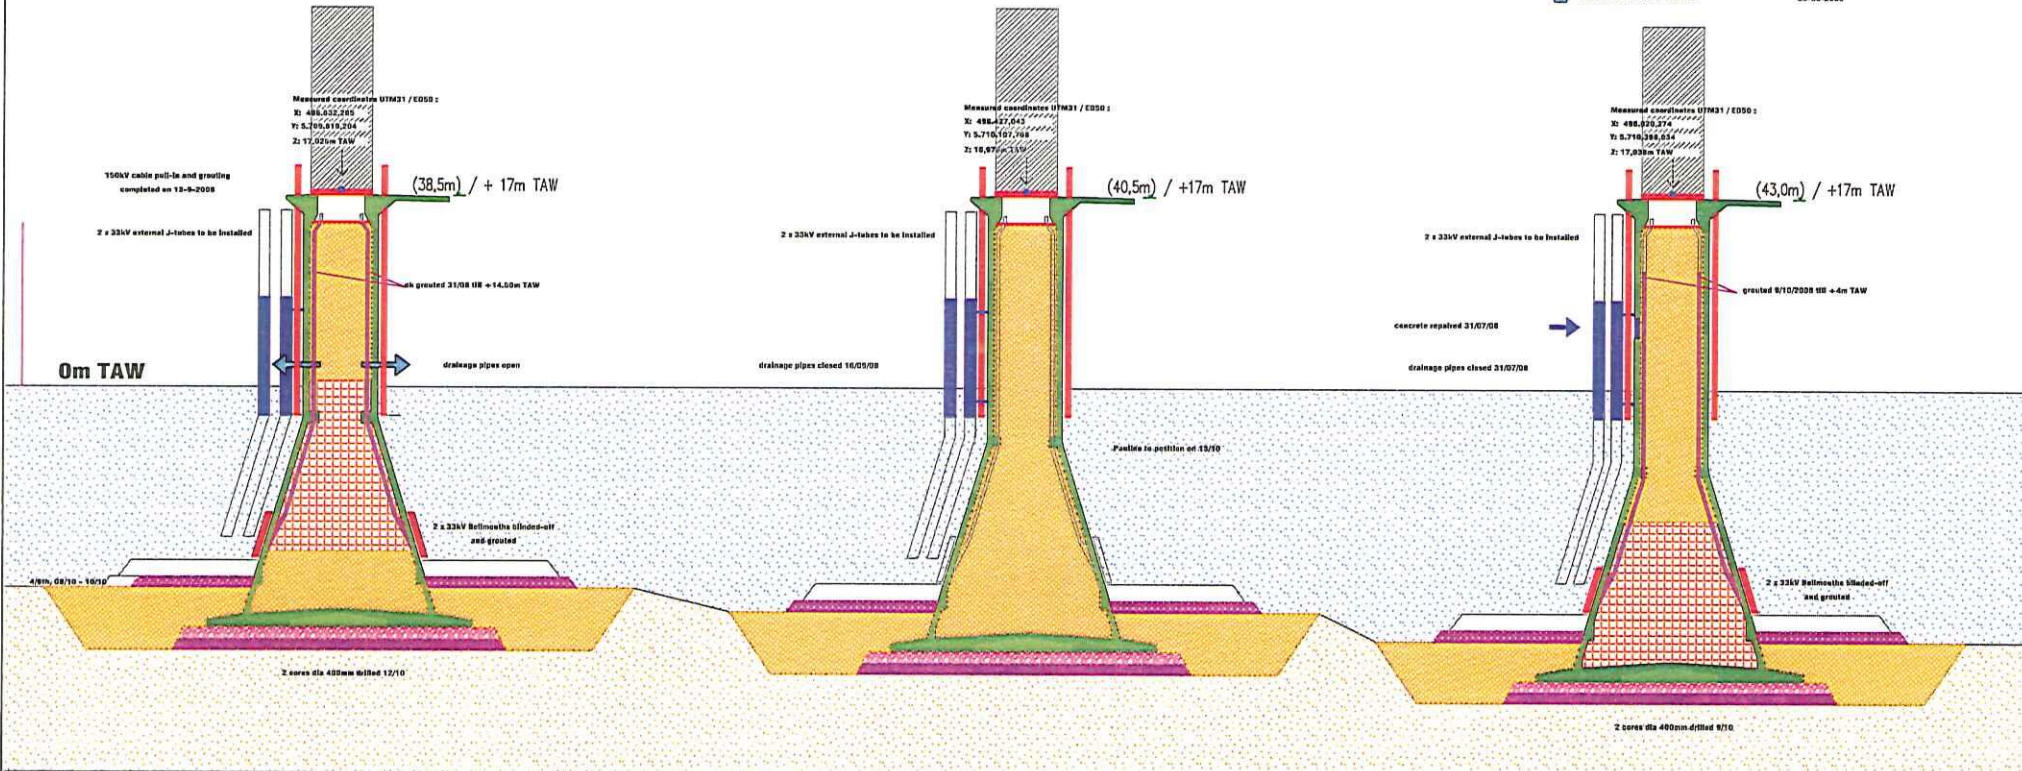

- Infill with big bags
- Infill with big bags (magna dense)
- Hydraulic infill
- Finalized
- Ongoing / Partially realized

Installation of GBF's at Thorntonbank situation on 13-10-2008

D4


	Completed as per DAN
Foundation pit bulk dredging	23-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	13-05-2008
Gravel bed top layer	17-05-2008
GBF installed	22/23-05-2008
Backfill	16-06-2008
Infill	25-07-2008
Scour protection filter layer	28-08-2008
Scour protection armour layer	
Armour layer on cables	
Ladders	18-08-2008
Leveling transition piece	18-08-2008
Dry infill of last 2m	17-08-2008
Fairly airtight floor	
service crane base	18-08-2008
Blind flange bellmouth	22-08-2008
Grouted J-tubes	25-09-2008
Repair works heat landing	
Installation external J-tubes	
Measurement Earth Resistance	28-08-2008

D5

	Completed as per DAN
Foundation pit bulk dredging	23-03-2008
Foundation pit precision dredging	4-04-2008
Gravel bed filter layer	9-05-2008
Gravel bed top layer	12-05-2008
GBF installed	30/31-05-2008
Backfill	11-06-2008
Infill	3-07-2008
Scour protection filter layer	31-08-2008
Scour protection armour layer	
Armour layer on cables	
Ladders	4-07-2008
Leveling transition piece	20-08-2008
Dry infill of last 2m	3-07-2008
Fairly airtight floor	
service crane base	20-08-2008
Blind flange bellmouth	28-08-2008
Installation external J-tubes	
Measurement Earth Resistance	30-08-2008

D6

	Completed as per DAN
Foundation pit bulk dredging	2-04-2008
Foundation pit precision dredging	5-04-2008
Gravel bed filter layer	6-05-2008
Gravel bed top layer	12-05-2008
GBF installed	28/29-05-2008
Backfill	14-06-2008
Heavy infill	22-06-2008
Sand infill	27-06-2008
Scour protection filter layer	28-08-2008
Scour protection armour layer	
Armour layer on cables	
Ladders	25-08-2008
Leveling transition piece	25-08-2008
Dry infill of last 2m	27-06-2008
Fairly airtight floor	
service crane base	25-08-2008
Blind flange bellmouth	11-10-2008
Installation external J-tubes	
Measurement Earth Resistance	30-08-2008

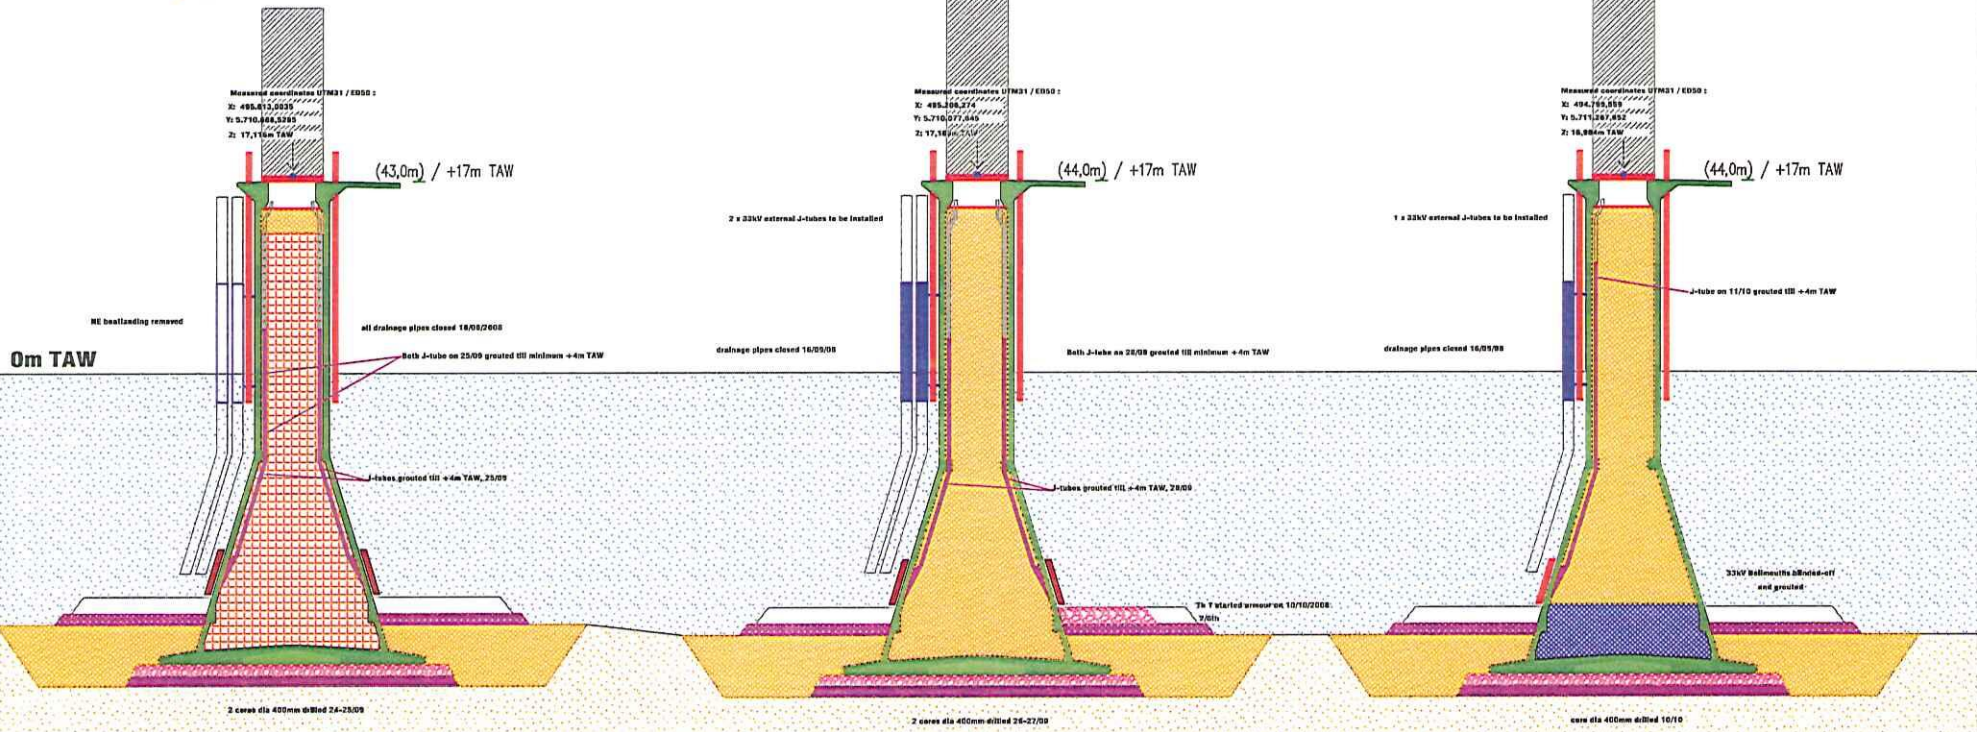

 Finalized	 Infill with big bags
 Ongoing / Partially realized	 Infill with big bags (magna dense)
	 Hydraulic infill
